




Minot International Airport

CONSTRUCTION NEWSLETTER: WEEK 23

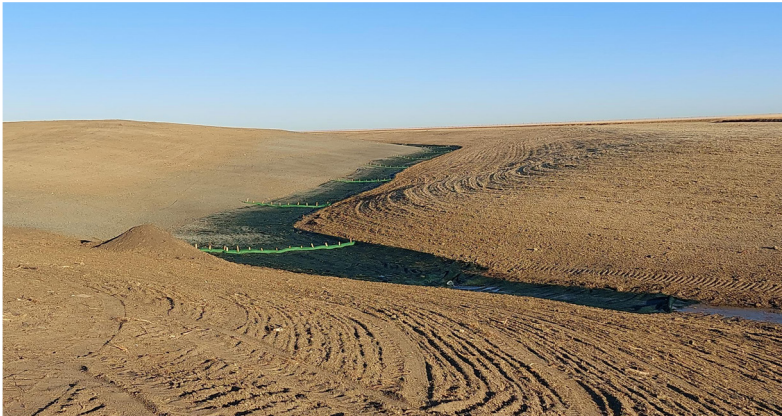

Contact Information:

Wildlife Hazard Removal

SEH Engineer

Jarrod Nelson, PE

651.325.8161

Airport Operations Manager

Maria Romanick

701.857.4724



This is the twenty third weekly newsletter update regarding the summer 2024 construction projects at Minot International Airport.

WILDLIFE HAZARD REMOVAL PROJECT

- Landscaping, seeding, and mulching work has been substantially completed in the Phase 1 area (southwest quadrant of the airport) and Phase 2 area (southeast quadrant of the airport).
- Phase 3 construction in the northeast quadrant of the airport is proceeding with airfield ditch grading, filling in of wetlands, topsoiling, and landscaping.
- Retention basin A storm sewer pipe installation continues at the south end of the airport.
- **Project Lookahead**
 - Next week, the contractor will continue Phase 3 topsoiling and landscaping. Retention basin A work will include storm sewer pipe installation, backfilling, and site restoration.
 - Project construction is anticipated to reach substantial completion across all phases by late-November, weather permitting.

Please check NOTAMs for up-to-date information regarding the airfield status.
