




# Minot International Airport

## CONSTRUCTION NEWSLETTER: WEEK 24

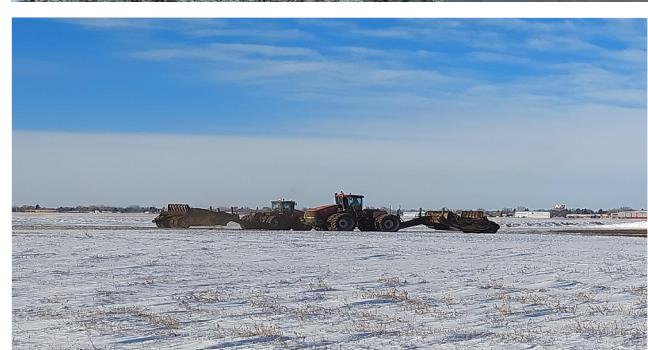

### Contact Information:

#### Wildlife Hazard Removal

SEH Engineer  
**Jarrod Nelson, PE**  
 651.325.8161

Airport Operations Manager  
**Maria Romanick**  
 701.857.4724



This is the twenty fourth weekly newsletter update regarding the summer 2024 construction projects at Minot International Airport.

### WILDLIFE HAZARD REMOVAL PROJECT

- Construction is substantially complete in the Phase 1 area (southwest quadrant of the airport) and Phase 2 area (southeast quadrant of the airport).
- The majority of Phase 3 earthwork construction in the northeast quadrant of the airport has been completed. Construction is being halted due to winter weather conditions.
- Retention basin A storm sewer pipe and impact structure have been installed. The remainder of backfill and restoration at the site is being halted due to winter weather conditions.
- Project Lookahead**
  - After November 21, construction operations will generally be halted until the Spring of 2025.
  - Spring construction efforts at the Phase 3 project site will include completion of drain tile installation, topsoil placement, and landscaping/turf establishment. Backfill and restoration of the Retention Basin A site will also be completed in the spring.

*Please check NOTAMs for up-to-date information regarding the airfield status.*
